



Engineering Services Manager's Report

Engineering and Operations Committee

Item 7b

June 12, 2017

Weymouth Oxidation Retrofit Program

Main Ozonation Facilities

- Notice of Completion filed - 5/24/17
- 14-day operating test commenced - 5/31/17
- Remaining work
 - Control system integration
 - Performance testing
 - Preparation of O&M manuals
 - Record drawings
- Anticipated date for use of ozone as primary disinfectant – Early fall 2017


Weymouth Oxidation Retrofit Program



Weymouth Oxidation Retrofit Program




Weymouth Oxidation Retrofit Program

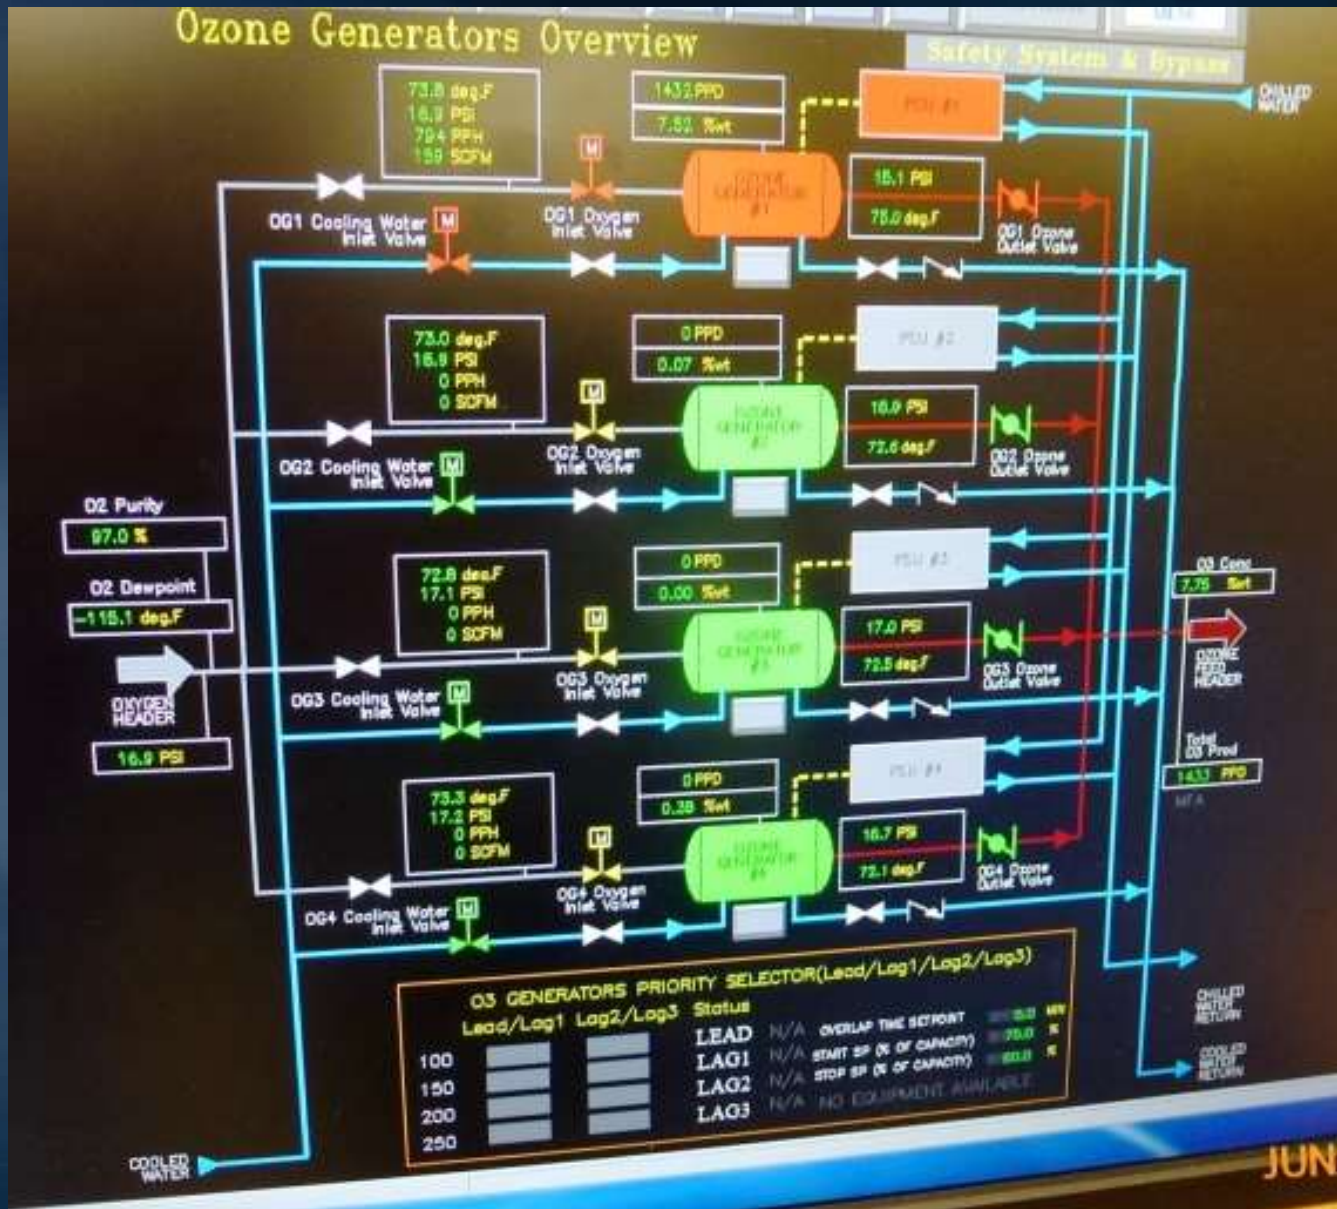

Weymouth Oxidation Retrofit Program



Weymouth Oxidation Retrofit Program

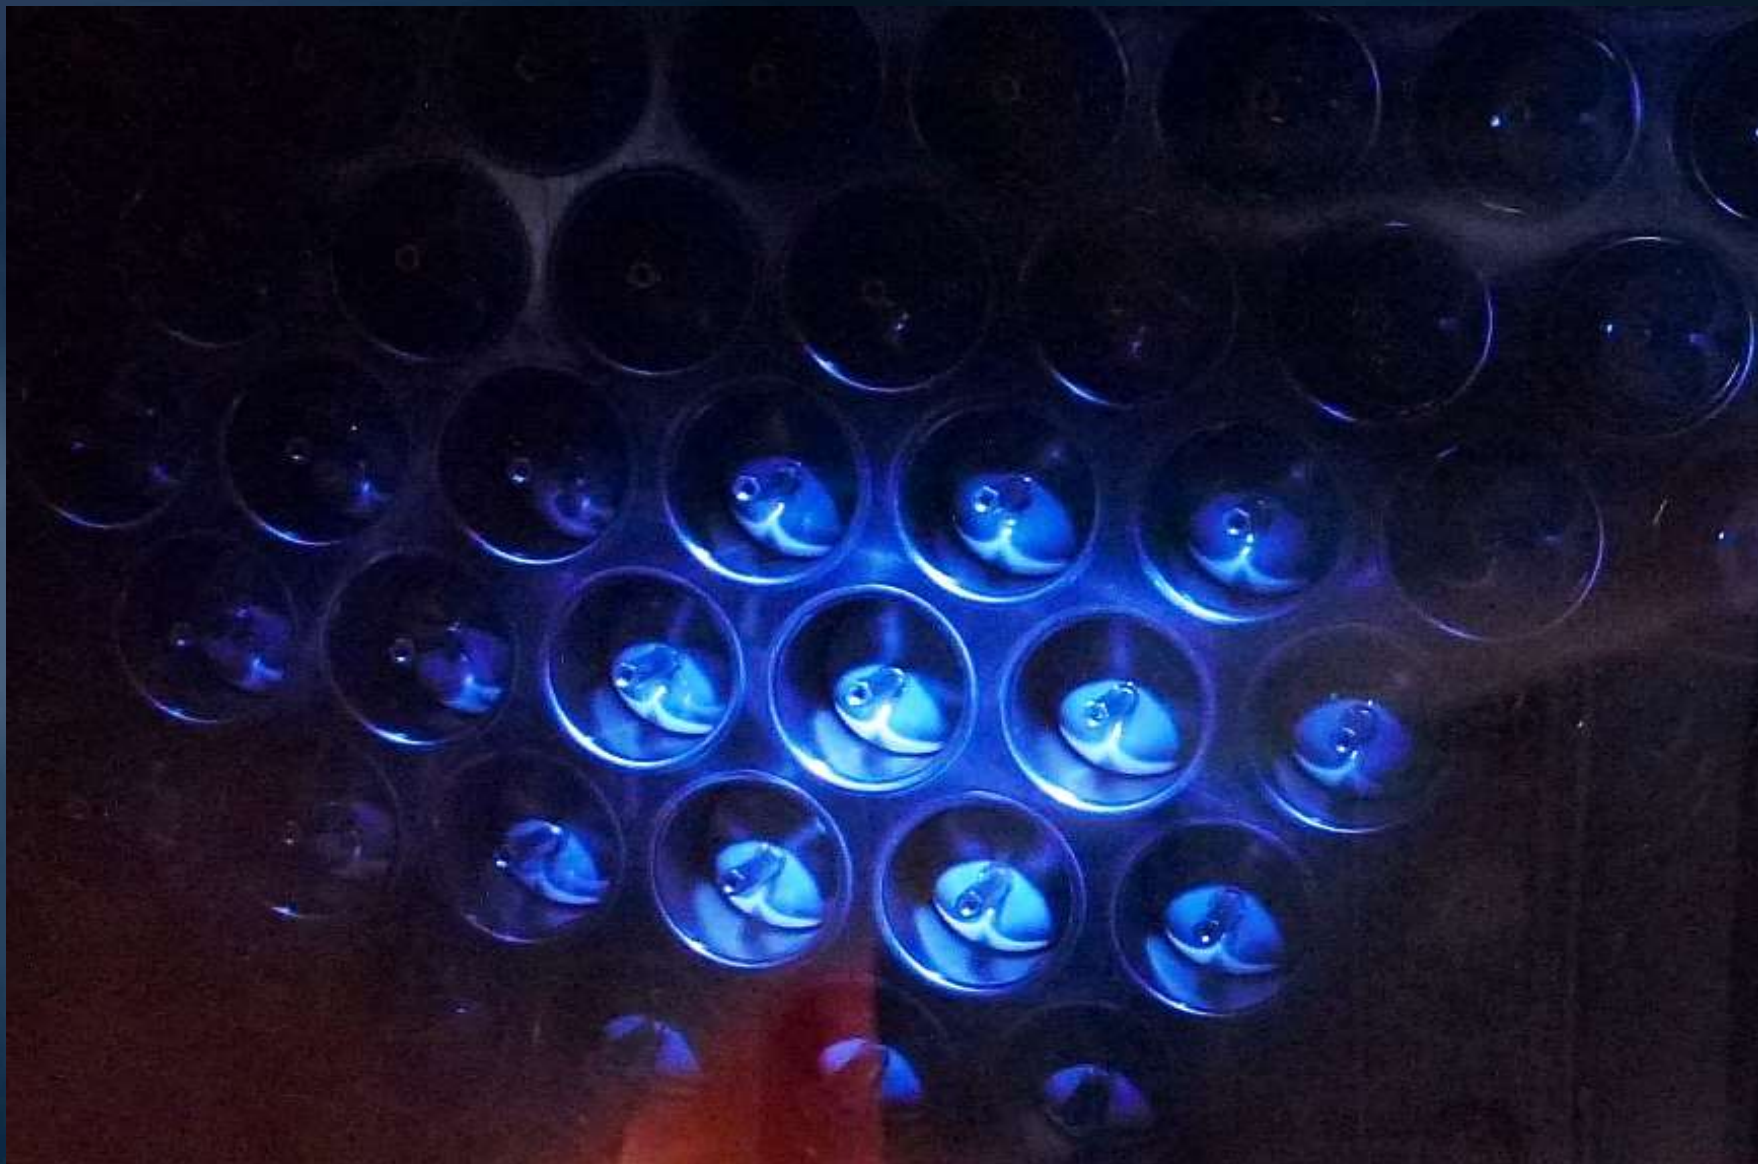

Weymouth Oxidation Retrofit Program

Chemical Feed Upgrades

- Construction currently 78% complete
- Scheduled completion – 06/18

Domestic Water System Improvements

- Construction currently 45% complete
- Scheduled completion – 08/17

Completion Activities

- Award of construction contract -12/17
(Final Board Action for ORP)

