



Information Technology Manager's Report

Organization, Personnel and Technology Committee

Item 7b


April 12, 2021

Datacenter Modernization Relocation Project Update - General Status

SECONDARY Datacenter	Status
Board Presentation	Completed
New Equipment and Services PO	Completed
New Site Contract	Completed
New Equipment Delivery	Completed
Old Equipment Move	80%
Network Installation and Configuration	90%
Applications Move	90%
Integrated System Testing	80%
Datacenter Move Completed	85%
Hand-off to MWD operations	4/19/2021

PRIMARY Datacenter	Status
Board Presentation	Completed
New Equipment and Services PO	In Process
New Site Contract	Completed
New Equipment Delivery	In Process
Old Equipment Move	0%
Network Installation and Configuration	0%
Applications Move	0%
Integrated System Testing	0%
Datacenter Move Completed	0%
Hand-off to MWD operations	3/31/2022

Backup Datacenter Timeline

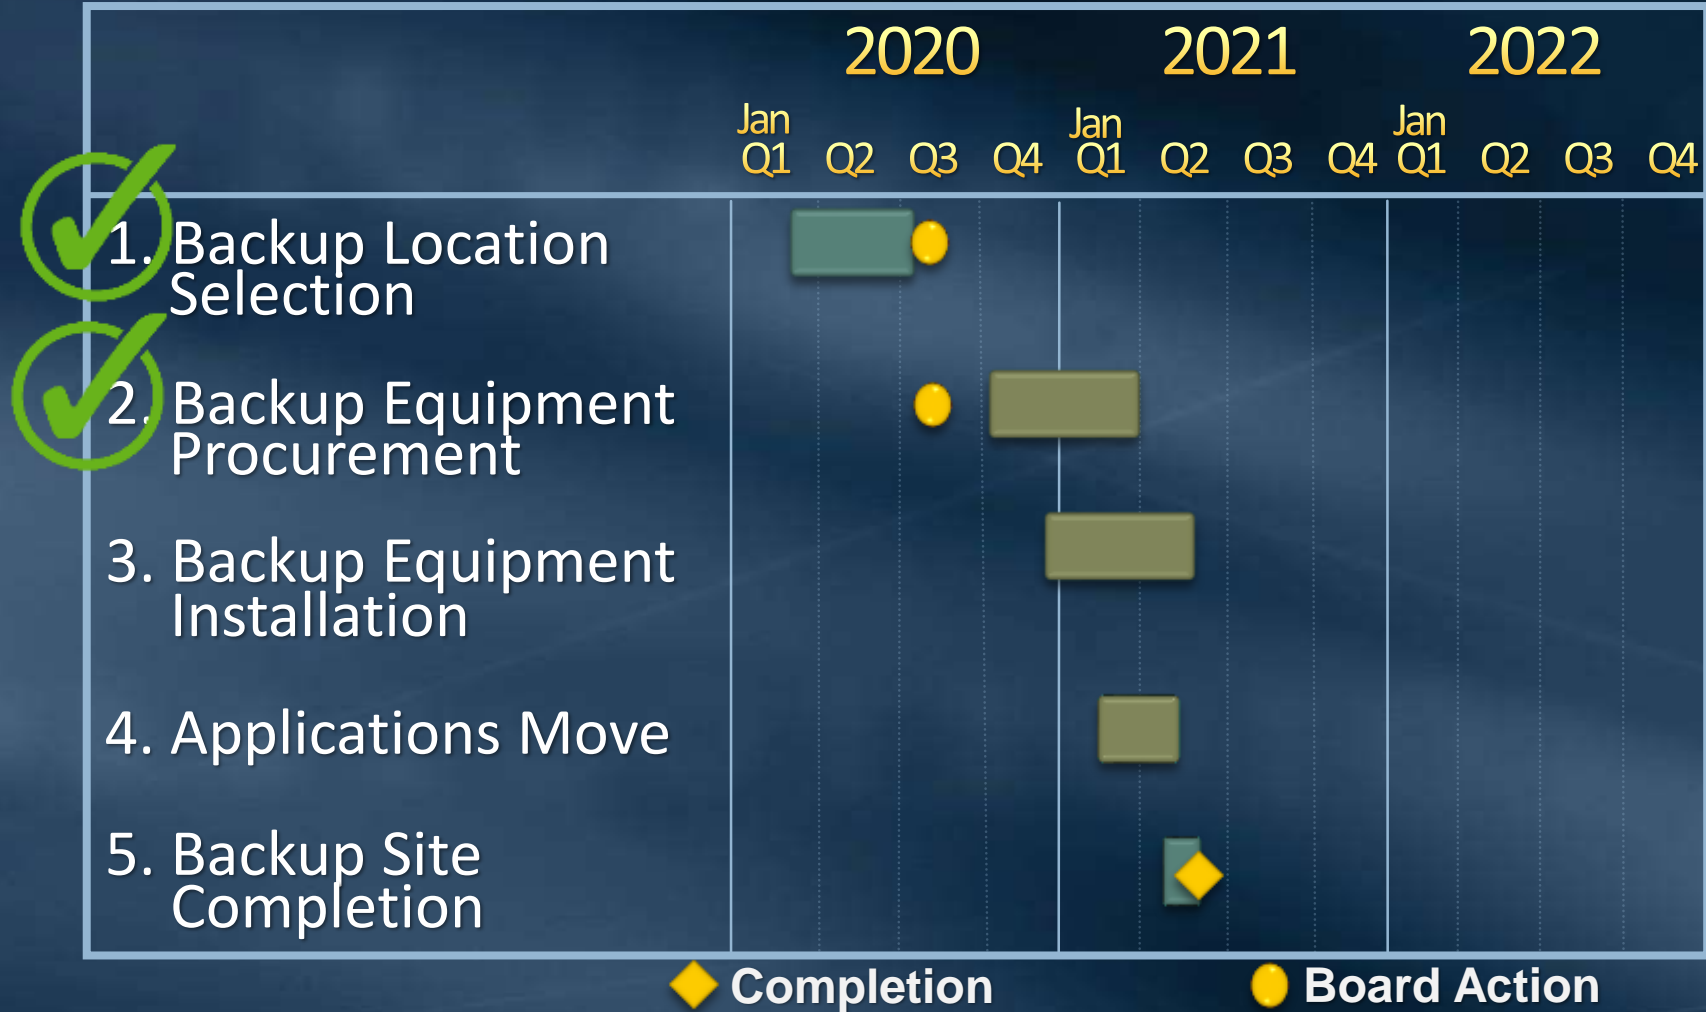

Primary Datacenter Timeline



