Engineering and Operations Committee Item #6b

Subject: CIP Quarterly Report

Purpose: To provide a progress update for the Fiscal Year 2012/13 Capital Investment Plan.

Engineering and Operations Committee Item #6b

Summary:

The Fiscal Year 2012/13 Capital Investment Plan has estimated expenditures of \$257 million spread over more than 350 projects. Maintain focus on reliability, safety, and regulatory driven projects. All projects are within budget.



#### Capital Investment Plan Quarterly Report Fiscal Year 2012/13

Engineering & Operations Committee Item 6b June 10, 2013


# Summary

- Over 350 projects underway
- Expenditures through March totaled \$94 million compared to a budget of \$173 million
- Currently 28 construction /procurement contracts
- Completed 17 contracts; \$25 million


#### CIP FY 2012/13 – Top 10 Projects

	2012/13 Budget	YTD Apr Actual
Weymouth ORP	\$ 52.6 M	\$17.3 M
Diemer ORP	15.5 M	11.6 M
La Verne Shops Upgrades	12.7 M	7.5 M
<b>PCCP</b> Rehabilitation (mult. projects)	5.8 M	<b>3.4 M</b>
Yorba Linda Power Plant	4.7 M	<b>1.6 M</b>
Weymouth Electrical Upgrades	<b>4.2</b> M	<b>3.2 M</b>
<b>CRA Copper Basin Outlet/Sluiceway</b>	<b>4.0 M</b>	<b>1.9 M</b>
CRA High Voltage Switches	<b>3.6 M</b>	<b>2.1 M</b>
CUF Chlorine Containment	<b>2.9</b> M	<b>2.2 M</b>
Eagle Rock/Puddingstone Gates	<b>2.8</b> M	3.2 M

#### **Project Locations**

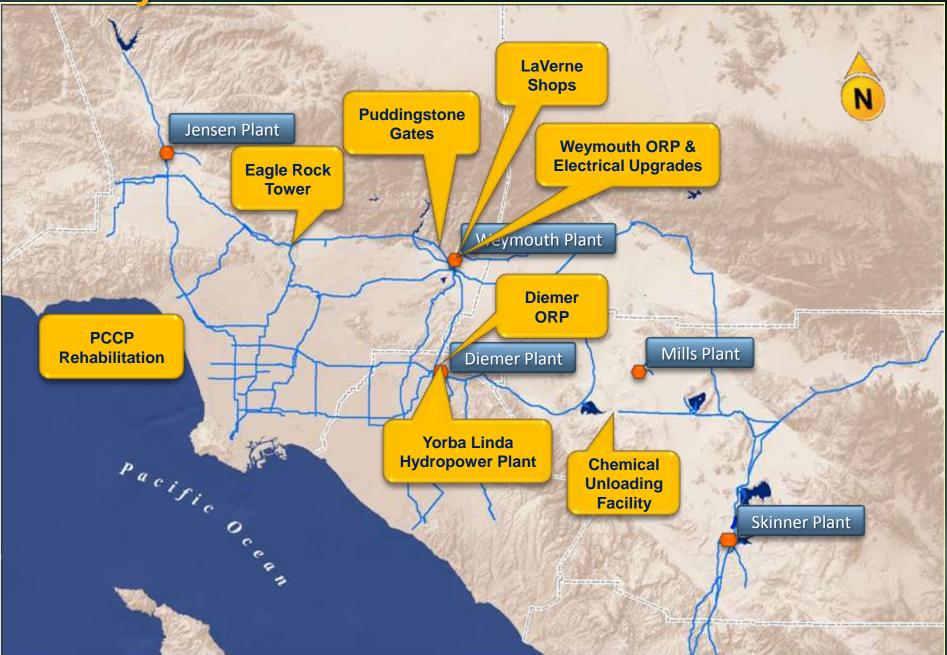

#### **CRA Project Location**

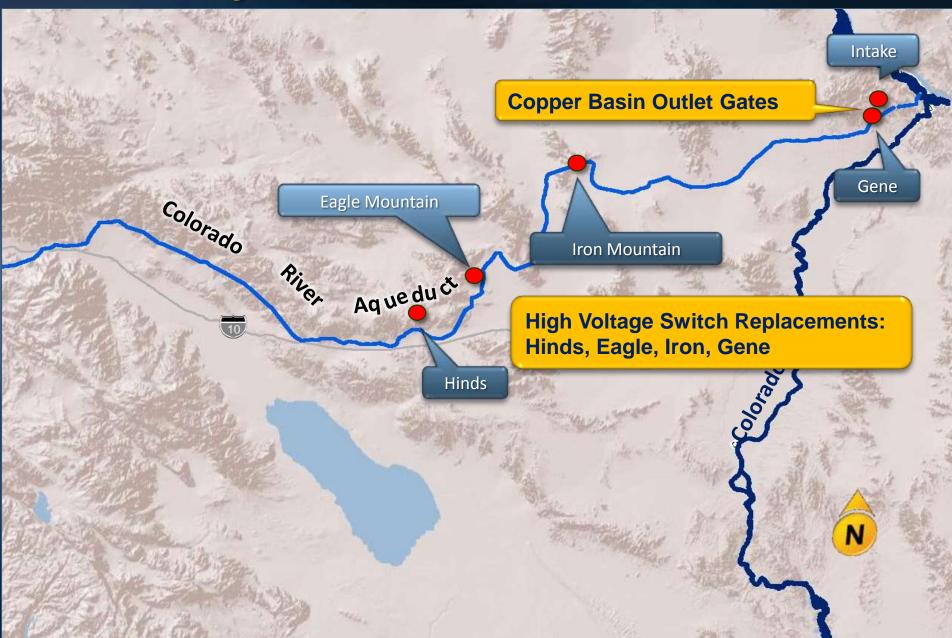


# Weymouth ORP

Appropriated Amount	% Complete (March 2013)	Budget Status
\$216,012,000	13%	Within budget



#### **Diemer ORP**

Appropriated Amount	% Complete (March 2013)	Budget Status
\$366,232,400	99%	Within budget

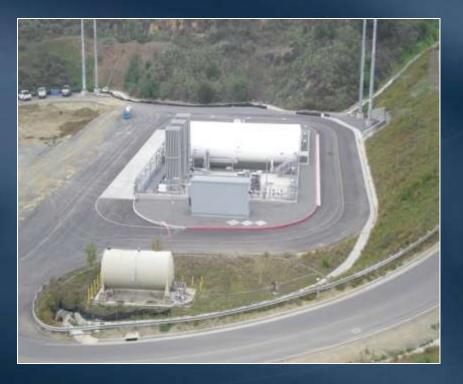



### La Verne Coating Shop Upgrades

Appropriated Amount	% Complete (March 2013)	Budget Status
\$9,237,700	99%	Within budget



### **PCCP** Rehabilitation

Appropriated Amount	% Complete (March 2013)	Budget Status
\$15,430,000	56%	Within budget



#### Yorba Linda Power Plant

Appropriated Amount	% Complete (March 2013)	Budget Status
\$8,925,000	80% (final design)	Within budget



## Weymouth Electrical Upgrades

Appropriated Amount	% Complete (March 2013)	Budget Status
\$37,781,000	99%	Within budget



#### **CRA Copper Basin Outlet**

Appropriated Amount	% Complete (March 2013)	Budget Status
\$6,916,000	35%	Within budget



## **CRA High Voltage Switches**

Appropriated Amount	% Complete (March 2013)	Budget Status
\$8,284,800	99%	Within budget



#### **CUF Chlorine Containment**

Appropriated Amount	% Complete (March 2013)	Budget Status
\$4,970,000	99% (final design)	Within budget



### Eagle Rock & Puddingstone Gates

Appropriated Amount	% Complete (March 2013)	Budget Status
\$4,684,800	98%	Within budget



### **Minor Capital Projects**

FY Budget	2008/09	2009/10	2010/11	2011/12	2012/13	2013/14
Amount appropriated	\$4.83	\$4.5 M	\$3.5 M	\$3 M	\$5 M	\$5 M
# of Projects	22	23	17	17	23	-
# of Projects Complete through March 2013	21	19	10	7	2	-
% of Work Complete	97%	93%	83%	61%	20%	-
Expenditures through March 2013	\$3.8 M	\$3.3 M	\$2.5 M	\$1.9 M	\$0.8 M	-

### **Moving Forward**

- Begin the CIP project evaluation process for the FY 2014/15 & FY 2015/16 biennial budget
- Collaborate with CFO to streamline the capital budget & appropriation process
- Plan for long-term, comprehensive rehabilitation programs within five year finance plan
- Maintain focus on reliability, safety & regulatory driven projects

