



# Engineering Services Manager's Report

Engineering & Operations Committee  
Item 7b  
July 8, 2019

# Engineering Services Group

## 2019 Engineer Interns

Name of Student	University	Name of Student	University
Gabriel Macias	Cal Poly Pomona	Cynthia Vo	UCLA
Steven Tullos	Cal Poly Pomona	Alex Sun	UCLA
Dion Mokhtari	Cal Poly Pomona	Oscar Tupul	CSU Los Angeles
Abel Yanez	Cal Poly Pomona	Mario Valdez	CSU Los Angeles
Miguel Maldonado	Cal Poly Pomona	Eric Saldivar	CSU Long Beach
Madeline Perez	Cal Poly Pomona	Kaden Springer	USC
Claire Turner	Cal Poly San Luis Obispo	Mikayla Ector	Hampton University
Jonathan Song	UC San Diego		

# Update on Projects at Diemer Plant



# Orange County Region Service Center

- Contract Award Date:  
March 2018
- Contract Amount:  
\$9,257,483
- Contractor:  
R.I.C. Construction, Inc.
- Percent Complete:  
47%
- Estimated Completion Date:  
February 2020




# Orange County Region Service Center Current Construction Activities



# Diemer West Basins & Filter Rehabilitation

- Contract Award Date  
**October 2018**
- Contract Amount:  
**\$38,539,196**
- Contractor:  
**Environmental Construction, Inc.**
- Percent Complete:  
**29%**
- Estimated Completion Date:  
**December 2020**

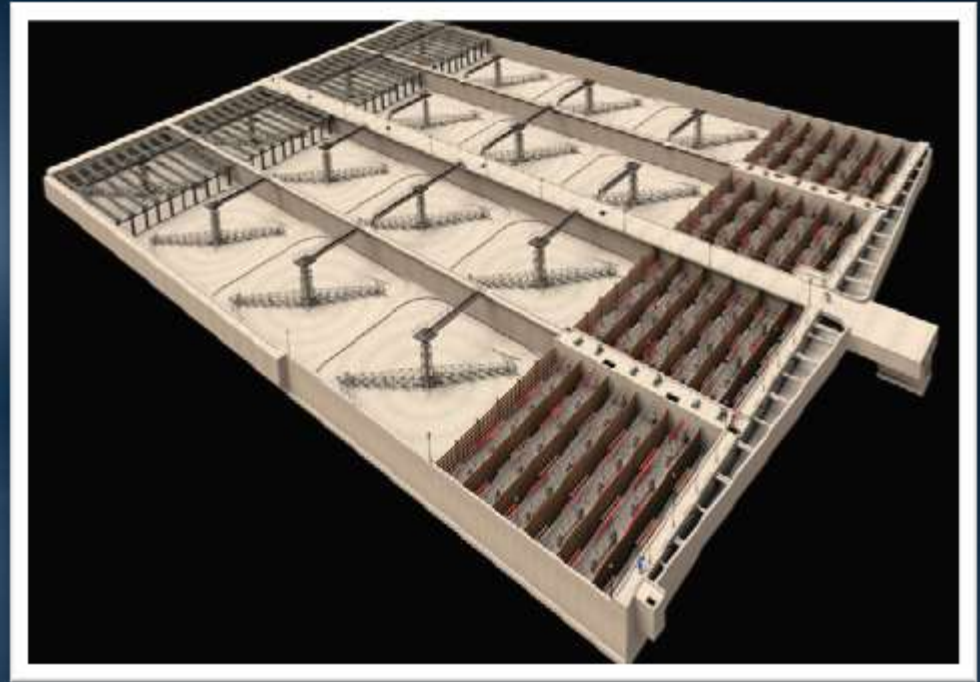

# Diemer West Basins & Filter Rehabilitation Current Construction Activities



# Skinner Outlet Tower Seismic Assessment Studies





# Skinner Outlet Tower Seismic Assessment Studies



