



Engineering Services Manager's Report

Engineering and Operations Committee

Item 7b

June 7, 2021

Construction and Procurement Contracts

April 2021

Construction & Procurement Contracts Through April 2021	
Number of Contracts at end of April 2021	38
Total Bid Amount of Contracts in Progress at end of April 2021	\$385M
Contracts Awarded in April 2021	0
Contracts With Notice To Proceed Issued in April 2021	0
Contracts Completed in April 2021	0
Contract Gross Earnings in April 2021	\$11.7M


West Valley Feeder No. 1 De Soto Ave Valve Structure Upgrades

- Contract Amount:
 - \$594,800
- MWD Force Costs to Date:
 - \$520,000
- Anticipated Completion Date:
 - June 30, 2021



Upgrades to Headquarters Building HVAC System

- Project Details:
 - Install ultraviolet (UV) light air disinfecting system in each of the building's 29 air handling units
 - Conduct work as a change order to existing building upgrades contract
 - Operational by December 2021

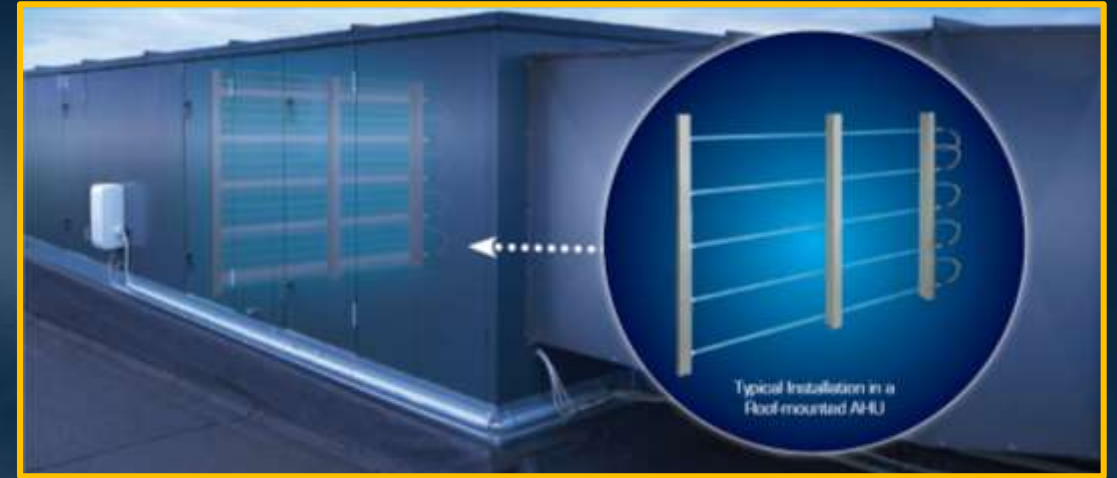

Typical UV light installation in air handling unit

F. E. Weymouth Water Treatment Plant Water Quality Instrumentation Improvements

- Contract Amount:
 - \$2,944,000
- Board Award:
 - August 2019
- Contractor:
 - Mehta Mechanical Company, Inc.
- Percent Complete:
 - 94 %



Existing Water Quality Instruments
in the Administration Building Basement

F. E. Weymouth Water Treatment Plant Water Quality Instrumentation Improvements



Installation of New Instrumentation and Panels

F. E. Weymouth Water Treatment Plant Water Quality Instrumentation Improvements



New Water Quality Instrumentation Building

2021 Member Agency Engineering Managers Forum

- Co-hosted by:
 - Calleguas Municipal Water District
- Date:
 - June 24, 2021
- Venue:
 - Virtual via Zoom



